

Look Ahead View for May 20th, 2019

There Is A Lot Of Progress to Show

Work continues inside the building, doing final cleaning and installing technology throughout the building. The building mechanical systems, which are all operational, are being balanced. We expect the climbing wall in the gym to be installed starting next week.

Work outside continues in many areas now that the weather has improved. The sign is going up on the building, landscaping is being installed and the bench seating for the exterior classrooms is approaching completion. Temporary roadwork is in progress and the construction fence is scheduled to be moved in a few weeks. Preparations are well underway to move the construction trailers to an area behind the current Clyde Brown School.

This is a particularly busy time for the construction team, wrapping up construction inside the new building and preparing punch lists for final acceptance, while preparing for the movement of staff from the existing school in June and the delivery of furniture. It is possible that the Elementary School Building Committee may elect to delay the Certificate of Occupancy until mid-June to allow more time to complete the building prior to final acceptance. This delay will not affect the schedule and will still allow the teachers to relocate to the new building immediately following the end of school on June 14th. Demolition of the old building, new traffic patterns and parking improvements have been planned and will begin in earnest as soon as the school year ends on June 14.

Updated pictures follow. You will see both interior and exterior photos showing the progress to completion. Things are changing daily on the site and it is very exciting to watch.

Planning for the ribbon cutting and dedication of the new school continues. Mark your calendars for September 7th!

Main Entrance



New Building Sign Installation



Look Ahead View for May 20th, 2019

Installing Sidewalks



Installing The Temporary Roadway



Gazebo and 3,4,5 Wing



Landscape Installation Outside 3,4,5 Wing



Outside Classroom Pre-K, K Wing



Outside Classroom 3,4,5 Wing



Look Ahead View for May 20th, 2019


Pre-K, K Wing



Pre-K, K Wing Entrance



Pre-K, K Wing Ready For Final Cleaning

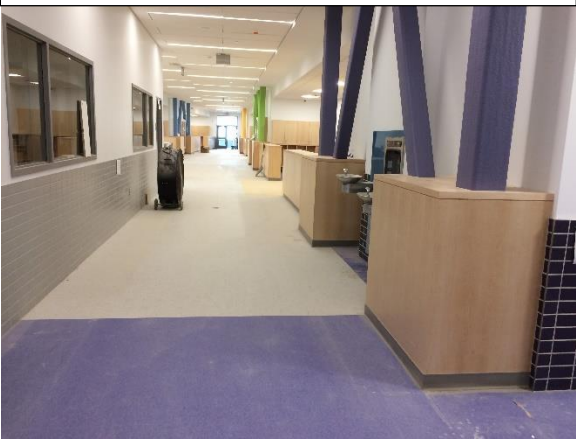

Gym Floor Logo




Finished Pre-School Classroom



Finished And Cleaned Classroom



Look Ahead View for May 20th, 2019

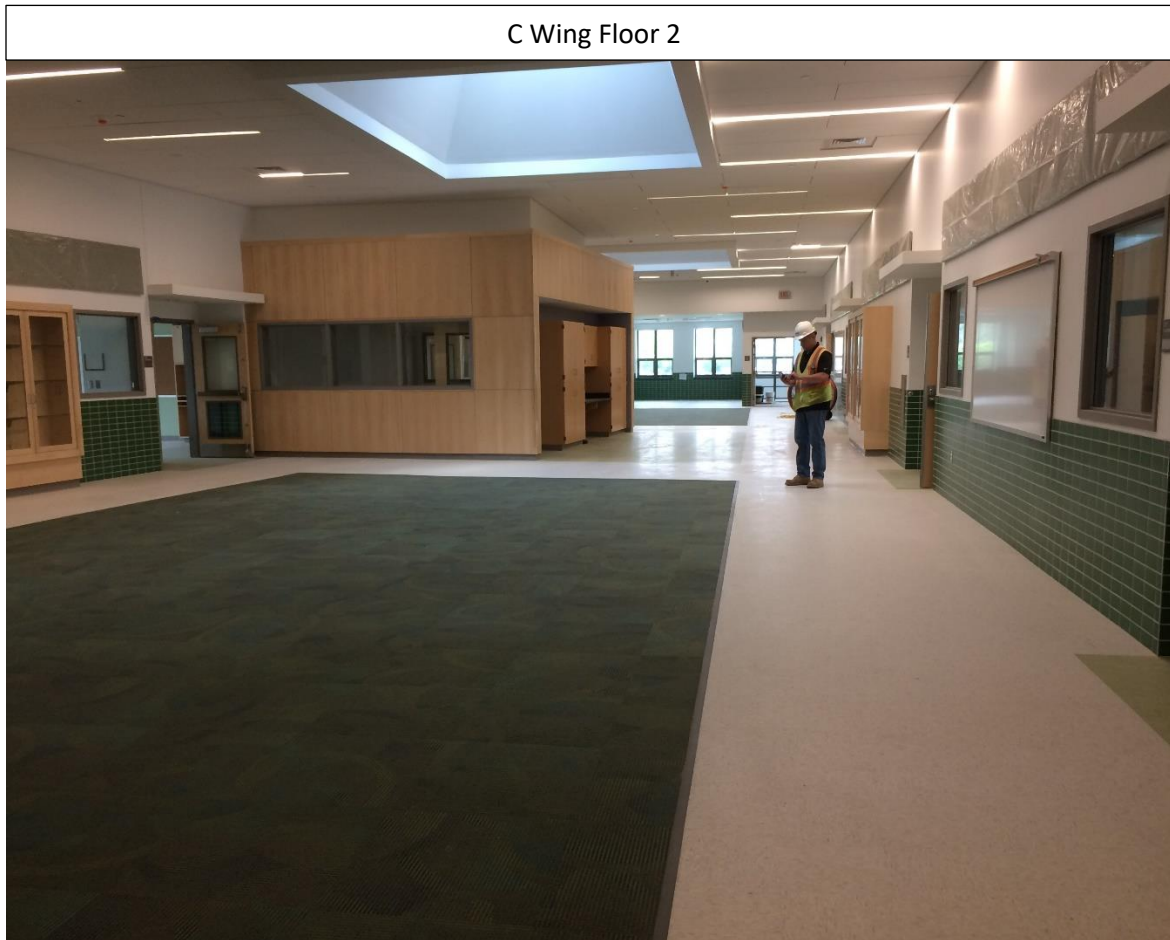

For more information about the New Elementary School project, follow us on:

www.Millis.Org Look on the front page under News and Notices for the current Look Ahead View and under Boards and Committees for the Elementary School Building Committee page to find prior Look Ahead Views.

www.Facebook.com/MillisSchoolProject/ Look for current posts about the project.

Or look on www.Facebook.com/MillisCommunityMedia for meeting videos.

www.MillisMedia.org Look under Videos for recordings of the Elementary School Building Committee meetings and other relevant events.

The Elementary School Building Committee
